

Bluffs ADA Proj.


Hyatt Contracting Inc.

Project Lead: David Hyatt

TASK	ASSIGNED TO	PROGRESS	START	END
Preconstruction, Planning, Design				
Submittals	David Hyatt	100%	5/28/25	5/28/25
Purchasing	Francisco Bejar	100%	5/30/25	5/30/25
Scheduling	David Hyatt	100%	6/2/25	6/2/25
Demo ADA Ramps				
Mobilizations	Brandon Niesen	0%	6/9/25	6/9/25
Ramp #1 5718 Summil David Hyatt		0%	6/9/25	6/9/25
Ramp #2 5730 Summit Dr.		0%	6/9/25	6/9/25
Ramp #3 5746 Summit Dr.		0%	6/9/25	6/10/25
Ramp #4 5747 Summit Dr.		0%	6/10/25	6/10/25
Ramp #5 5751 Summit Dr.		0%	6/13/25	6/13/25
Ramp #6 5752 Summit Dr.		0%	6/13/25	6/13/25
Ramp #7 5729 Terrace Rd.		0%	6/16/25	6/18/25
Ramp #8 5737 Terrace Rd.		0%	6/16/25	6/18/25
Ramp #9 5749 Terrace Rd.		0%	6/16/25	6/18/25
Ramp #10 5757 Terrace Rd.		0%	6/16/25	6/18/25
Ramp #11 5769 Terrace Rd.		0%	6/16/25	6/18/25
Ramp #12 5777 Terrace Rd.		0%	6/19/25	6/20/25
Ramp #13 5788 Terrace Rd.		0%	6/19/25	6/20/25
Ramp #14 3411 Stoney Rd.		0%	6/19/25	6/20/25
Ramp #15 Stanford Ranch N.		0%	6/25/25	6/25/25
Ramp #15 Stanford Ranch S.		0%	6/26/25	6/26/25
Ramp #17 3420 Stoney Rd.		0%	6/26/25	6/26/25
Ramp #18 3422 Stoney Rd.		0%	6/26/25	6/27/25
Ramp #19 5806 Ford Rd.		0%	6/30/25	7/1/25
Ramp #20 5812 Ford Rd.		0%	6/30/25	7/1/25
Ramp #21 3400 Rockford Ct.		0%	6/30/25	7/2/25

Project start: Wed, 5/28/2025

Display week: 1

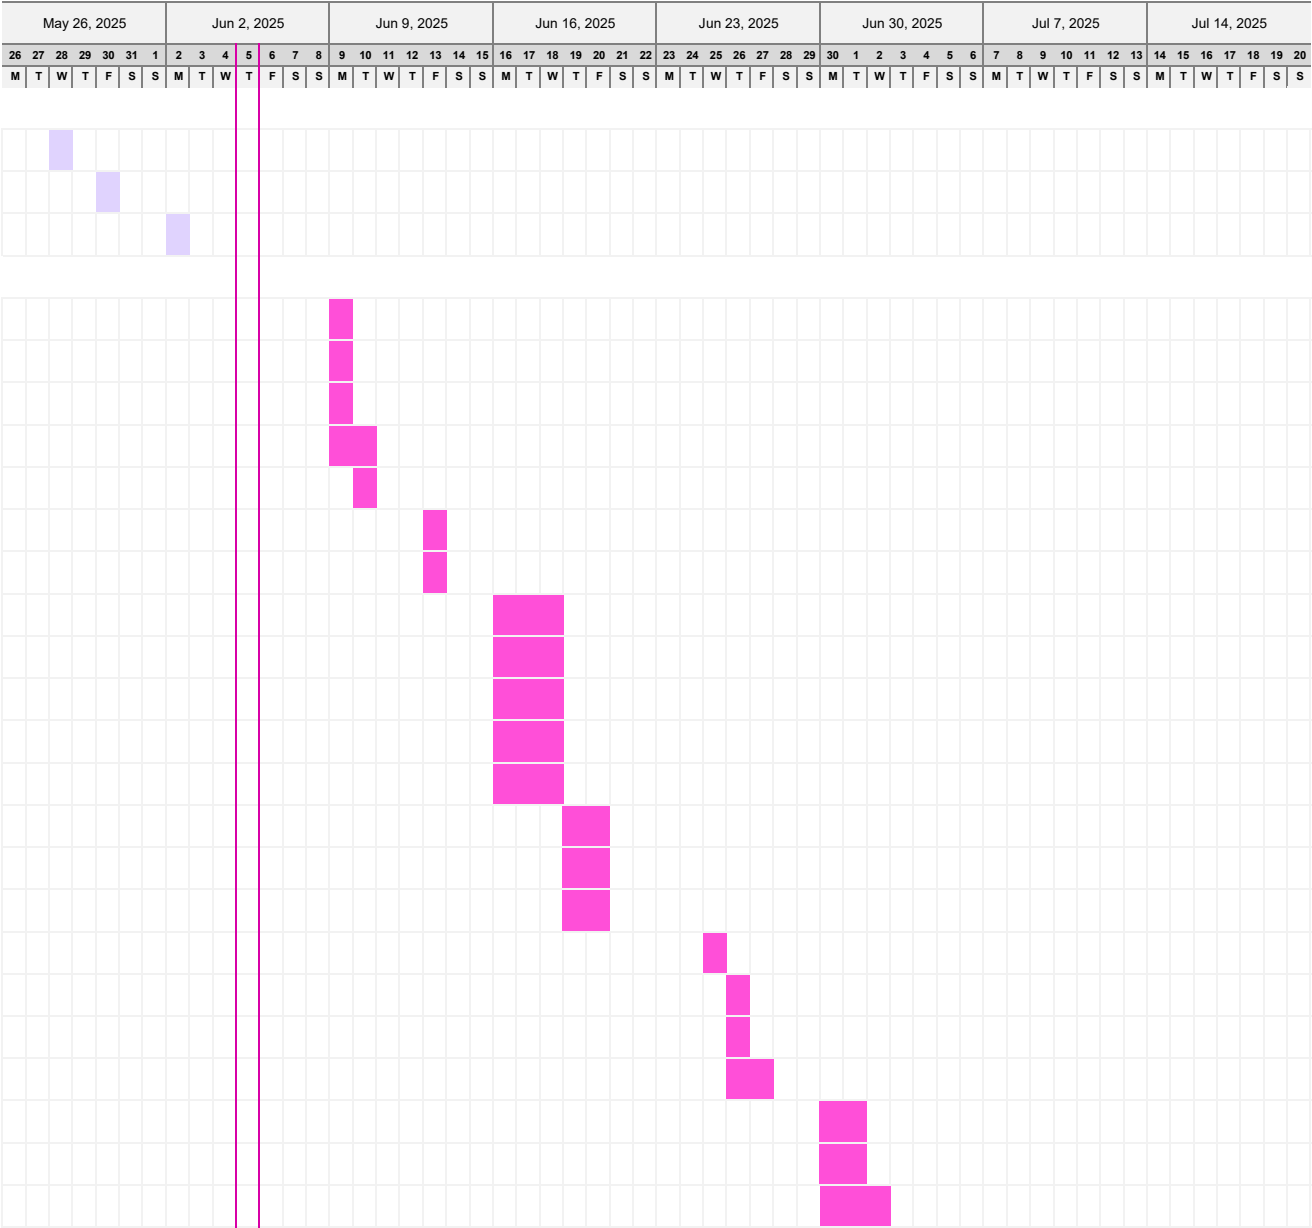

TASK	ASSIGNED TO	PROGRESS	START	END
Ramp #22 3401 Rockford Ct.		0%	6/30/25	7/2/25
Ramp #23 5829 Ford Rd.		0%	7/7/25	7/10/25
Ramp #24 5831 Ford Rd.		0%	7/7/25	7/10/25
Ramp #25 5076 Midas Ave.		0%	7/7/25	7/10/25
Ramp #26 5075 Midas David Hyatt		0%	7/7/25	7/10/25
Construct ADA Ramp				
Ramp #1 5718 Summil Gonzalo Suchil		0%	6/10/25	6/13/25
Ramp #2 5730 Summit Dr.			6/10/25	6/13/25
Ramp #3 5746 Summit Dr.			6/10/25	6/14/25
Ramp #4 5747 Summit Dr.			6/10/25	6/14/25
Ramp #5 5751 Summit Dr.			6/16/25	6/20/25
Ramp #6 5752 Summit Dr.			6/16/25	6/20/25
Ramp #7 5729 Terrace Rd.			6/16/25	6/20/25
Ramp #8 5737 Terrace Rd.			6/16/25	6/20/25
Ramp #9 5749 Terrace Rd.			6/16/25	6/20/25
Ramp #10 5757 Terrace Rd.			6/16/25	6/20/25
Ramp #11 5769 Terrace Rd.			6/16/25	6/20/25
Ramp #12 5777 Terrace Rd.			6/23/25	6/24/25
Ramp #13 5788 Terrace Rd.			6/23/25	6/24/25
Ramp #14 3411 Stoney Rd.			6/23/25	6/24/25
Ramp #15 Stanford Ranch N.			6/25/25	6/25/25
Ramp #16 Stanford Ranch S.			6/26/25	6/26/25
Ramp #17 3420 Stoney Rd.			6/27/25	6/27/25
Ramp #18 3422 Stoney Rd.			6/30/25	6/30/25
Ramp #19 5806 Ford Rd.			6/30/25	7/3/25
Ramp #20 5812 Ford Rd.			6/30/25	7/3/25
Ramp #21 3400 Rockford Ct.			6/30/25	7/3/25
Ramp #22 3401 Rockford Ct.			6/30/25	7/3/25
Ramp #23 5829 Ford Rd.			7/7/25	7/9/25
Ramp #24 5831 Ford Rd.			7/7/25	7/9/25
Ramp #25 5076 Midas Ave.			7/7/25	7/9/25
Ramp #26 5075 Midas Ave			7/7/25	7/9/25

